



Obsolete Pesticides Management Project (P131778)

AFRICA | Cote d'Ivoire | Environment & Natural Resources Global Practice |
Global Environment Project | Specific Investment Loan | FY 2016 | Seq No: 2 | ARCHIVED on 07-Jun-2016 | ISR23871 |

Implementing Agencies: Ministry of Environment, Urban Health and Sustainable Development

Key Dates

Key Project Dates

Bank Approval Date:25-Aug-2015

Effectiveness Date:19-Jan-2016

Planned Mid Term Review Date:20-Aug-2018

Actual Mid-Term Review Date:--

Original Closing Date:30-Oct-2020

Revised Closing Date:30-Oct-2020

Global Environmental Objectives

Global Environmental Objective (from Project Appraisal Document)

The Project Development Objective (PDO) is to improve the management of obsolete pesticides and associated wastes in Côte d'Ivoire by the Government and other stakeholders.

Has the Global Environmental Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Regulatory and institutional framework:(Cost \$1.90 M)

Management of obsolete pesticides and associated wastes:(Cost \$6.50 M)

Promotion of alternatives to chemical pesticides:(Cost \$0.70 M)

Project management:(Cost \$1.70 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of GEO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Substantial	● Substantial



Implementation Status and Key Decisions

The project was signed on October 20 2015 and became effective on January 19 2016. It was launched on 2 February 2016 in a ceremony chaired by the Minister of the Environment, Hon. Rémi Allah-Kouadio. The first six months of the project have been characterized by unusually long delays in meeting effectiveness conditions and completing a first withdrawal application. It is too early for any project activities to have begun so the project is still in a start-up phase. An implementation support mission is planned for the week starting 4 July 2016 to more fully evaluate the status of the project and agree on corrective measures to speed up project implementation.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Moderate	● Moderate	● Moderate
Macroeconomic	● Low	● Low	● Low
Sector Strategies and Policies	● Low	● Low	● Low
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate



Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Moderate	● Moderate	● Moderate
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Moderate	● Moderate	● Moderate
Other	--	--	--
Overall	● Substantial	● Substantial	● Substantial

Results

Global Environmental Objective Indicators

▶ Data on OPs and associated wastes publicly accessible(Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	80.00
Date	01-Jul-2015	--	--	30-Oct-2020

▶ POPs&pops waste destroyed,disposed or contained in environmentally sound manner(Metric ton, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	250.00
Date	01-Jul-2015	--	--	30-Oct-2020

▲ OPs and associated waste safely contained at targeted sites(Metric ton, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	100.00
Date	01-Jul-2015	--	--	30-Oct-2020



▲ OPs and associated waste safely disposed of(Metric ton, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	150.00
Date	01-Jul-2015	--	--	30-Oct-2020

▶ Direct project beneficiaries(Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	100000.00
Date	01-Jul-2015	--	--	30-Oct-2020

▲ Female beneficiaries(Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	50.00

Overall Comments

A first progress report is still pending so no updated information on the baselines or actual measurements of any of the indicators. No project activities have commenced.

Intermediate Results Indicators



► National strategy for management of OPs and associated wastes implemented (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0	--	--	3
Date	01-Jul-2015	--	--	30-Oct-2020

► Pesticides Committee functional (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1.00	--	--	3.00
Date	01-Jul-2015	--	--	30-Oct-2020

► Effective regulatory framework for obsolete pesticides and associated wastes (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3.00
Date	01-Jul-2015	--	--	30-Oct-2020

► Inventory of obsolete pesticides and associated wastes (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3.00
Date	01-Jul-2015	--	--	30-Oct-2020



► MIS on obsolete pesticides and associated wastes established and functional (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3.00
Date	01-Jul-2015	--	--	30-Oct-2020

► Implementation of pilots on alternatives to chemical pesticides (Number, Custom)


	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	3.00
Date	01-Jul-2015	--	--	30-Oct-2020

Overall Comments

A first progress report is still pending so no updated information on the baselines or actual measurements of any of the indicators. No project activities have commenced.

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P131778	TF-A0742	Effective	USD	7.00	7.00	0.00	0.43	6.57	 6%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P131778	TF-A0742	Effective	25-Aug-2015	20-Oct-2015	19-Jan-2016	30-Oct-2020	30-Oct-2020

Cumulative Disbursements

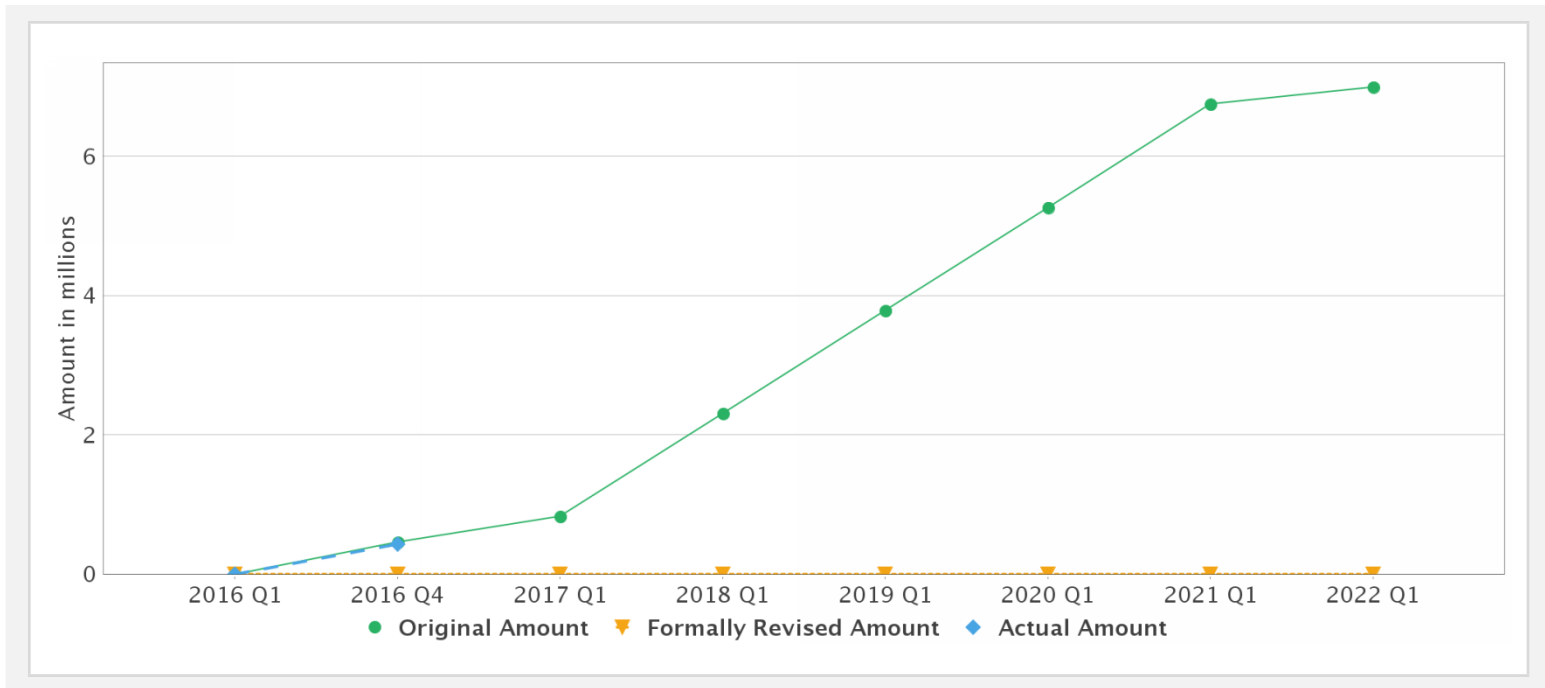

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
