



## DRC Street Children Project (P115318)

AFRICA | Congo, Democratic Republic of | Social Protection Global Practice |  
IBRD/IDA | Specific Investment Loan | FY 2010 | Seq No: 8 | ARCHIVED on 10-Jun-2015 | ISR19700 |

Implementing Agencies:

### Key Dates

#### Key Project Dates

Board Approval date:01-Jun-2010

Effectiveness Date:28-Feb-2011

Planned Mid Term Review Date:06-Jan-2014

Actual Mid-Term Review Date:21-Feb-2014

Original Closing Date:31-Aug-2015

Revised Closing Date:31-Aug-2015

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective for this project is to improve the delivery mechanisms of prevention and support services for street children, primarily in Kinshasa.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

A: Prevention:(Cost \$3.10 M)

B: Assistance:(Cost \$4.30 M)

C: Capacity building, coordination and project management:(Cost \$2.60 M)

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	--	● Substantial



## Implementation Status and Key Decisions

Overall project performance continues to be satisfactory. As of June 1st, 2015 the disbursement rate is 92.22%, and the remaining funds are projected to be completely disbursed by project closing date of August 31, 2015. Performance indicators have continued to progress regularly and have reached or surpassed projections (see results framework). Over 15,524 children have benefited from project activities, and efforts at family reunification continue to yield very encouraging results with 4426 children (48 percent of them girls) having re-established links with their families.

The latest implementation support mission have confirmed that the PIU has adopted the following recommendations to contribute to project sustainability:

1. building the capacity of its partners: in April 2015 the PIU organized a workshop for all project stakeholders to reflect on ways to make project results sustainable. In response to the main concern expressed with funding, in May 2015 the PIU hosted a five-day training to develop the capacity of both government and NGOs to raise funds. The training was very well received.
2. contracting a consultant to produce a practitioner guide for family reunification on the basis of best practices and lessons learned during project implementation. The guide, expected by June 30, 2015, should be disseminated country-wide. As funds and time constraints will not permit the thorough dissemination process carried out for the Norms and Standards to Care for Children in Difficult Circumstances, it was agreed that the PIU would explore opportunities for collaboration with other projects including the USAID-financed 4Children Program.
3. signing an agreement with the National Institute of Statistics to carry out the third and last round of an impact evaluation of the project's preventive activities. Data collection was completed on schedule and statistical analysis is ongoing with assistance from the UNICEF/ILO/World Bank "Understanding Children's Work Project". A report is expected by mid-July and should be widely disseminated as it represents a unique opportunity to learn about prevention (there are very few evaluations of prevention services worldwide).

In anticipation of project closing, both the project implementation unit and the World Bank will start elaborating an implementation completion report. This document reflects on project performance and impact, and provides lessons learned to all parties involved.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	--	● High
Macroeconomic	--	--	● Substantial
Sector Strategies and Policies	--	--	● Substantial
Technical Design of Project or Program	--	--	● Low
Institutional Capacity for Implementation and Sustainability	--	--	● Substantial
Fiduciary	--	--	● Substantial
Environment and Social	--	--	● Moderate
Stakeholders	--	--	● Low
Other	--	--	--
Overall	--	--	● Substantial



## Results

### Project Development Objective Indicators

#### ► Direct project beneficiaries (Number, Core)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	13932.00	15524.00	--
Date	--	30-Jun-2014	31-Mar-2015	--

#### Comments

Including 9709 children (in the street or at risk, 3847 local authorities and community leaders, and 376 members of NGOs/CBOs. In addition, 15,322 households that have been exposed to sensitizations sessions are not included in this value.

#### ▲ Female beneficiaries (Percentage, Core Supplement)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	25.00	50.00	47.00	--

#### ▲ Children supported by type of services (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	9709.00	10057.00	8000.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

#### ▲ Community leaders and authorities sensitized (Number, Custom Breakdown)



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3847.00	74715.00	800.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

▲ NGOs, CBOs and Government workers trained (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	376.00	376.00	650.00
Date	--	31-Dec-2013	31-Mar-2015	31-Aug-2015

▶ Street children having restored relationships with their families (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	253.00	2516.00	4099.00	800.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

▶ Street Children offered access to comprehensive support services (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1103.00	7130.00	10057.00	5500.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

▶ Children at-risk provided with education or remedial education opportunities financed under the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2579.00	5467.00	2500.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015



► Target households who recall correctly key messages about children rights from the campaigns financed under the project (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	87.00	87.00	70.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

Comments

No new data was provided as of March 2015

► Child Protection Committees that are active (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	75.00
Date	--	30-Jun-2014	31-Mar-2015	--

Overall Comments

**Intermediate Results Indicators**

► Annual evaluation of the effectiveness and direct costs of different prevention and support services (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Partially done	Partially done	Yes
Date	--	24-Oct-2014	31-Mar-2015	31-Aug-2015



- A database established to monitor and coordinate ongoing children rights interventions as well as to capture the number of beneficiaries per category of service is established (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	Yes	Yes	Yes
Date	--	24-Oct-2014	31-Mar-2015	31-Aug-2015

- National standards for service delivery to street children developed and validated (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	None	Yes	Yes	Yes
Date	--	24-Oct-2014	31-Mar-2015	31-Aug-2015

- NGOs/FBOs and specialized public services supported by the project achieving at least 90% of the agreed performance indicators (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	--	--	--	70.00
Date	--	24-Oct-2014	31-Mar-2015	31-Aug-2015

Comments  
No data available

- Street Children benefitting from (i) skills, (ii) training, (iii) formal education (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	--	4689.00	7954.00	--
Date	--	30-Jun-2014	31-Mar-2015	--

Comments  
1660 professional training; 3679 formal education and 2615 non formal education



▲ Street children benefitting from skills (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	937.00	1660.00	6741.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

▲ Street Children benefitting from formal and non formal education (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3752.00	6294.00	6784.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

▶ Community events on children's rights and parental responsibility (e.g. interactive theatre) number per year (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	629.00	921.00	150.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

Comments

596 radio shows, 292 theater performances, 488 sensitization meetings

▶ Child Protection Committees (i) established (number) (ii) and/or strengthened (number) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	89.00	127.00	--
Date	--	30-Jun-2014	31-Mar-2015	--



#### ▲ child protection committee established (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	22.00	75.00	72.00
Date	--	30-Jun-2014	31-Mar-2015	31-Mar-2015

#### ▲ child protection committee strengthened (Number, Custom Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	67.00	52.00	62.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015

#### ▶ Radio broadcasts on child protection (number per year) (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	220.00	596.00	120.00
Date	--	30-Jun-2014	31-Mar-2015	31-Aug-2015


#### Comments

This is the cumulative figure, not annual. Through the end of the year 2014, the number was 457.

#### Overall Comments

## Data on Financial Performance

### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P115318	IDA-H5780	Effective	XDR	6.60	6.60	0.00	6.09	0.51	 92%


### Key Dates (by loan)





Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P115318	IDA-H5780	Effective	01-Jun-2010	14-Jul-2010	28-Feb-2011	31-Aug-2015	31-Aug-2015

**Cumulative Disbursements**

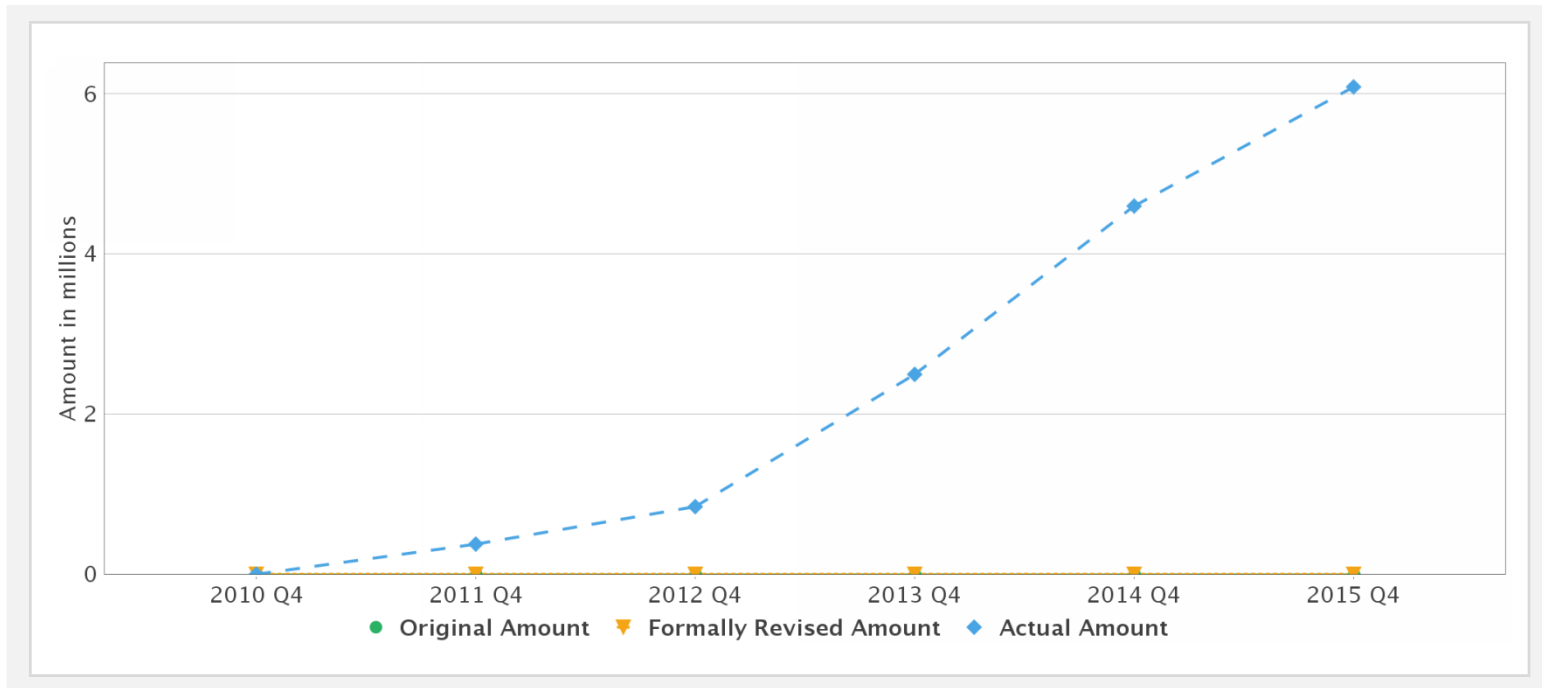

**Restructuring History**

Level 2 Approved on 13-Aug-2014

**Related Project(s)**

P124370-Enhancing DRC's Crisis Response for Street Children and other Vulnerable Groups
